DRIVEWAY RENOVATION STUDY

36 Squires Path

East Hampton, NY 11937

SCTM 300-184-2-9.1 Lot 6, Fox Hollow Estates 0.502 acres (21,901 sf)

Built 1972

Encroachment Status: RESOLVED — Written clearance obtained from Andrew Drake, Dept. of Land Acquisition & Management. Property is clear to proceed with permit applications.

Site Plan

Interactive property diagram — select an option below to see the proposed layout. Survey by Gary Benz, L.S. (May 2021).

A: Wide Court + Detached Garage ★ | B: Attached Garage | C: Carport (Phase 1) | D: Compact Court

☑ Setback Lines ☐ Existing Driveway ☑ Dimensions

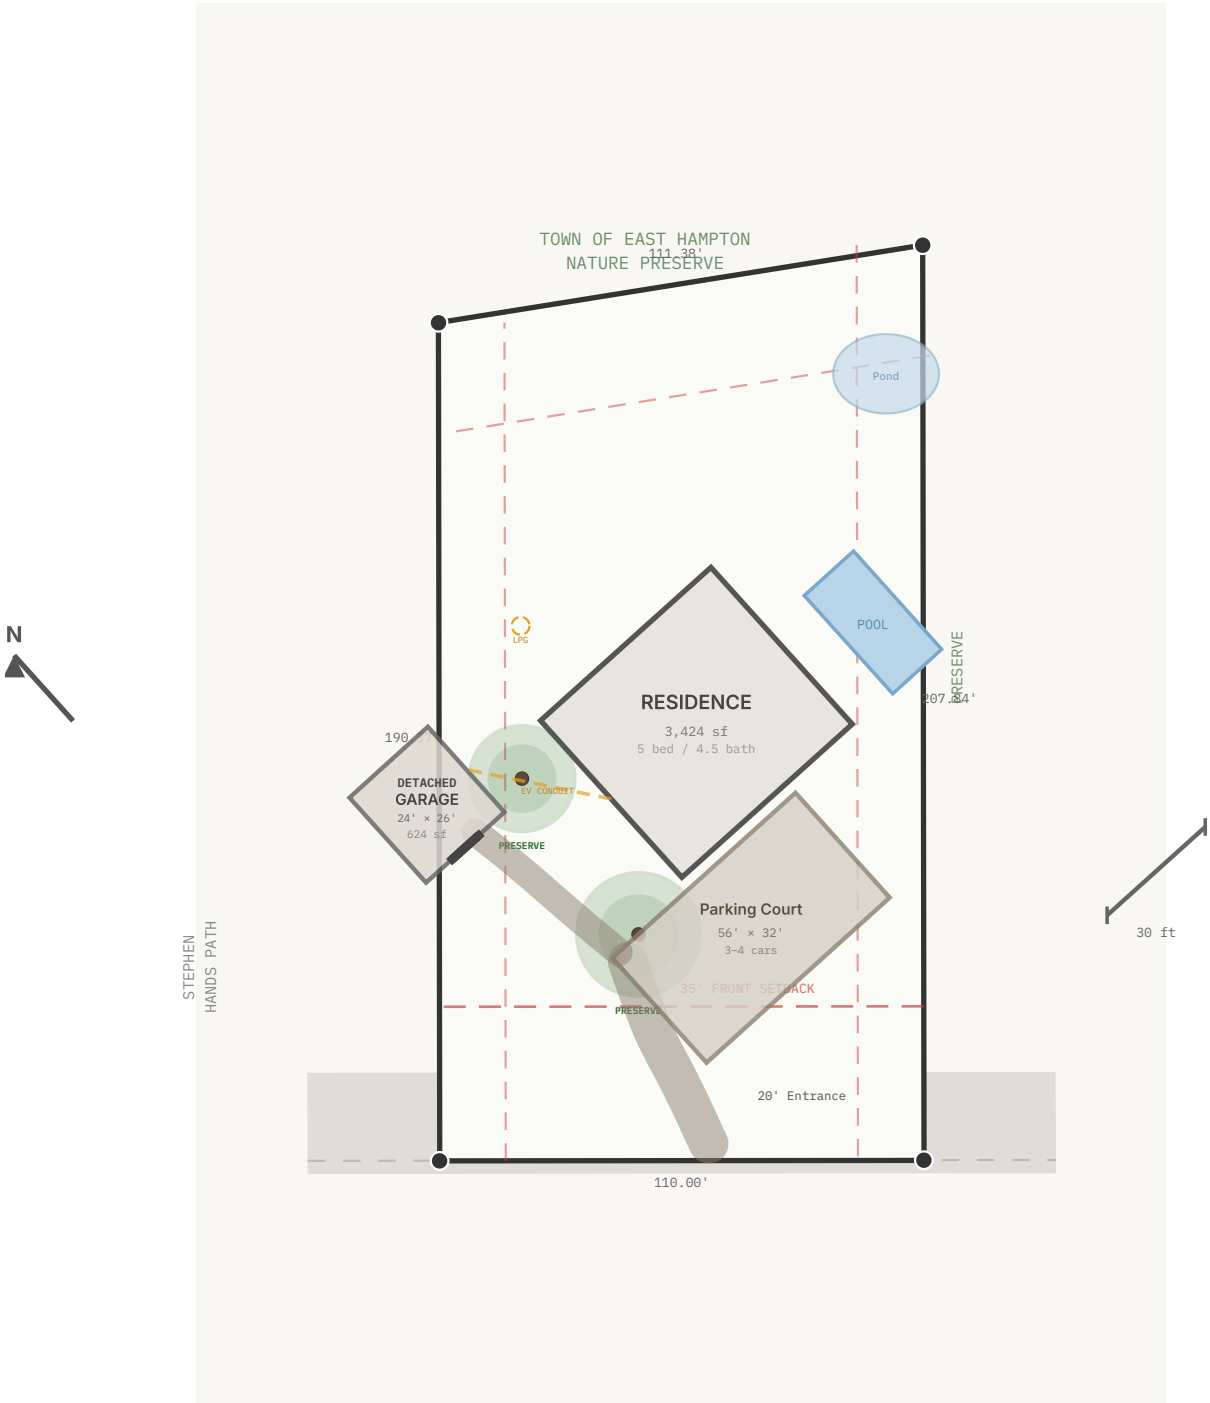

★ RECOMMENDED

Wide Court + Detached Garage

Large rectangular parking court in front of the house with a detached 2-car garage on the west side. Single wide entrance from Squires Path. Trees preserved as natural court features.

Court	56' × 32' (1,792 sf)
Capacity	3–4 cars

Garage	24' × 26' detached (624 sf)
Variance Risk	Low
Phases	1
Timeline	12–20 weeks

Building Coverage 13.9% / 20% max

Lot Coverage 29.2% / 50% max

Option Comparison

Side-by-side comparison of all four layout configurations.

Feature	A: Wide Court + Detached ★	B: Attached Garage	C: Carport (Phase 1)	D: Compact Court
Entrance Width	20'	20'	20'	18'
Parking Court	56' × 32' (1,792 sf)	56' × 32' (1,792 sf)	56' × 32' (1,792 sf)	42' × 28' (1,176 sf)
Car Capacity	3–4 cars	3–4 cars	3–4 cars	2–3 cars
Garage Type	Detached (624 sf)	Attached (672 sf)	Carport → Garage (576 sf)	Detached (572 sf)
Zoning Class	Accessory	Principal	Accessory	Accessory
Variance Risk	Low	None	Lowest	Low
Building Coverage	13.9% (of 20% max)	14.1%	13.7%	13.7%
Lot Coverage	29.2% (of 50% max)	29.4%	28.9%	26.1%
Phases	1	1	2	1
Timeline	12–20 wks	14–24 wks	Ph1: 10–16, Ph2: 4–8	14–22 wks

Feature	A: Wide Court + Detached ★	B: Attached Garage	C: Carport (Phase 1)	D: Compact Court
EV Ready	Conduit (30')	Conduit (15')	Phase 2	Conduit (50')

Zoning Analysis

Town of East Hampton, Chapter 255. All options well within coverage limits.

Coverage Calculations

Building Coverage (existing) 2,422 sf (11.1%)

0 sf Max: 4,380 sf (20%)

Lot Coverage (existing) 3,969 sf (18.1%)

0 sf Max: 10,951 sf (50%)

Remaining capacity:
Building: 1,958 sf available
Lot: 6,982 sf available

All four options fit comfortably within limits.

Setback Requirements

Front (Squires Path)	35'
Side — West (toward Lot 38)	15'
Side — East (preserve)	15'
Rear (preserve)	25'
Accessory side/rear setback	10'
Min separation (garage–house)	10'

Detached Garage (Accessory)

- Max 600 sf gross floor area
- Must be behind front building line
- Max height: 15' flat / 20' gabled
- Min 10' from dwelling
- No habitable space or plumbing
- Side/rear setbacks: 10–15'

Applies to Options A, C, D

Attached Garage (Principal Structure)

- No 600 sf cap — limited by coverage only
- Must meet principal structure setbacks
- Front: 35', Sides: 15', Rear: 25'
- Requires architectural plans
- Can include interior door to house
- Combined footprint ≤ 20% building coverage

Applies to Option B

Variance Argument (if needed)

If the garage placement requires a ZBA variance, the five-factor test is favorable:

1. **Reasonable Return:** Only home on Squires Path without covered vehicle storage. Diminishes utility and resale.
2. **Unique Hardship:** Nature Preserve on two sides eliminates ~50% of buildable envelope. Not shared by neighbors.
3. **Neighborhood Character:** Under 600 sf, matching architecture. Multiple neighbors have garages. Screened by landscaping.
4. **Not Self-Created:** Preserve boundaries set in 1968 subdivision. Owners purchased 2021 with pre-existing constraints.
5. **Minimum Variance:** Smallest feasible garage. Property stays at ~14% building coverage vs 20% max.

ZBA: 159 Pantigo Road, (631) 324-4143. Typical timeline: 2–4 months.

Surface Materials

Pricing reflects East End Long Island, Q1 2026. Select a material to update cost estimates below.

Belgian Block

$22–38 / sf

100+ year lifespan. Classic Hamptons aesthetic. Premium option.

Excellent Drainage | Heritage

Concrete Pavers / Bluestone

$15–28 / sf

Wide variety of patterns. Good balance of aesthetics and cost.

Good Drainage | Versatile

Asphalt

$7–15 / sf

Most cost-effective. Fast install. Smooth surface.

Budget | Poor Drainage

Crushed Stone / Gravel

$4–10 / sf

Lowest cost. Fully permeable. Casual East End feel.

Best Drainage | Lowest Cost

Attribute	Belgian Block	Pavers / Bluestone	Asphalt	Gravel
Cost / sf	$22–38	$15–28	$7–15	$4–10
Lifespan	100+ years	25–50 years	15–25 years	Indefinite
Install Time	2–3 weeks	1–2 weeks	3–5 days	2–4 days
Drainage	Excellent	Good	Poor	Excellent
Hamptons Fit	Perfect	Very Good	Common	Good — casual
Maintenance	Re-sand joints 3–5yr	Re-sand + seal 2–3yr	Seal-coat every 2–3yr	Regrade 1–2x/yr
Snow Removal	Good (plow-safe)	Good	Excellent	Difficult

Cost Breakdown

Estimates for each option with selected surface material. Costs reflect East End Long Island Q1 2026 pricing.

Selected material: **Belgian Block (Granite Cobble)** — click a material card above to change.

	Configuration	Low Estimate	High Estimate
★ Option A	Wide Court + Detached Garage	$72,124	$132,896
Option B	Wide Court + Attached Garage	$77,624	$141,896
Option C	Wide Court + Carport (Phase 1)	$61,624	$113,396
↳ Phase 2	Carport → Garage enclosure	+$10,000	+$25,000
Option D	Compact Court + Extended Drive	$58,372	$109,088

Estimates are approximate ranges. Actual costs depend on contractor selection, material availability, and site conditions. Get 3+ contractor bids before committing. Costs exclude variance fees ($5K–$12K) if applicable.

Project Timeline

Critical path: Attorney → Architect → Permit → Construction → Inspection. Typical total: 18–20 weeks.

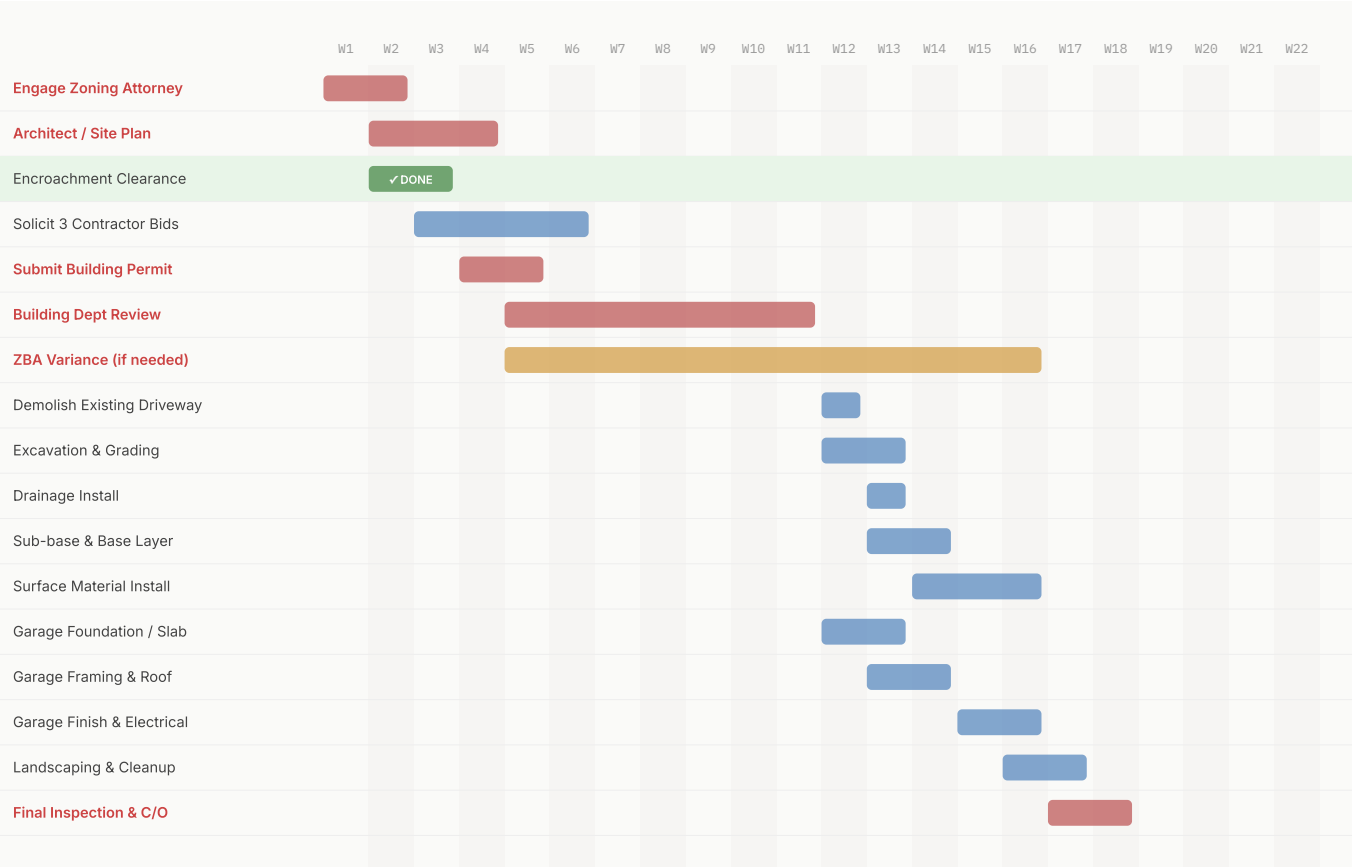

Best Case

12 weeks

No variance, fast permit review

Typical

18–20 weeks

Standard permit timeline

Worst Case

28–32 weeks

Variance required + summer delays

Garage vs. Carport

Enclosed Garage

Structure Cost	$12K–$22K
Weather Protection	Full
Security	Locked
Storage	Yes — enclosed
Property Value Impact	+$15K–$30K
Permit Complexity	Standard building permit
EV Charging	Conduit run at build

Open Carport

Structure Cost	$6K–$12K
Weather Protection	Roof only (open sides)
Security	Open
Storage	Limited — exposed
Property Value Impact	+$5K–$10K
Permit Complexity	Simpler — may not need full permit
Phase 2 → Garage	+$10K–$25K

Attached vs. Detached Garage

Detached Garage

Zoning Class	Accessory Structure
Size Limit	600 sf max

Setbacks	10' side/rear
Construction Impact	None to house
Placement Flexibility	More flexible
Weather Walk	Exposed walk to house

Attached Garage

Zoning Class	Principal Structure
Size Limit	No cap (coverage only)
Setbacks	35' front, 15' side, 25' rear
Construction Impact	Ties into house structure
Convenience	Interior door access
Cost Premium	+20–40% vs detached

Recommended Professionals

Zoning Attorneys

Twomey, Latham, Shea, Kelley, Dubin & Quartararo
Premier East End zoning firm. Riverhead. suffolklaw.com

Sill & Sill
Smaller firm, residential zoning in East Hampton

Contractors

J.A. Land Development
Full-service hardscape: driveways, cobblestone, bluestone, grading

All Purpose Paving (NY)
Family-owned, East End. nyallpurposepaving.com

APM O'Neill & Sons
30+ years East Hampton. (631) 480-3238

Town Contacts

Building Department
300 Pantigo Place, Suite 104. (631) 324-4142

Zoning Board of Appeals
159 Pantigo Road. (631) 324-4143

Land Acquisition — Andrew Drake
159 Pantigo Road. (631) 324-7420. adrake@ehamptonny.gov

Surveyor

Gary Benz, L.S.
Surveying and Land Planning
527-B Hawkins Avenue, Ronkonkoma, NY 11779
(631) 648-9348 | GaryBenzLS@Yahoo.com

2021 survey is valid (less than 10 years old)

Critical Path — Next Steps

1. **Engage Zoning Attorney**
   Determine if variance is needed for garage placement. Twomey Latham or Sill & Sill recommended. Week 1–2.

2. **Engage Architect for Site Plan**
   1/4" scale plans required for permit application. Must show clearing envelope. Week 2–4.

✓ ~~**Get Encroachment Clearance Letter**~~
DONE — Written resolution obtained from Andrew Drake.

3. **Solicit 3 Contractor Bids**
   Get bids from J.A. Land Development, All Purpose Paving, APM O'Neill. Can run concurrent with permitting. Week 3–6.

4. **Submit Building Permit**
   Two sets of plans, contractor signature (notarized), insurance cert, survey. Week 4–5.

5

Begin Construction

After permit approval (6–8 week review). Demo → excavation → base → surface → garage → landscaping. 4–6 weeks.

36 Squires Path Driveway Renovation Study
Prepared March 2026

Survey: Gary Benz, L.S. (May 2021)
SCTM 300-184-2-9.1

This document is for planning purposes only. All setback distances, coverage calculations, and zoning rules should be verified with the Town of East Hampton Building Department before filing any permit applications. Cost estimates are approximate ranges based on Q1 2026 East End pricing.
